



Colour Bricks

Construction Project Financial Management System

Business Requirement Document

Prepared For: Colour Bricks

Prepared By: Livewires Digital Solutions

Version: 1.1

Date: 27 August 2026

Status: Initial Requirement – For Client Review





Table of Contents

1. Introduction
2. Business Objectives
3. Application Modules
4. Project Management
5. Project Dashboard
6. Project Income / Credits
7. Project Expenses / Debits
8. Labour & Subcontractor Management
9. Subcontractor / Team Master
10. Labour / Subcontractor Work
11. Vendor Management
12. Vendor Master
13. Automatic Vendor Creation
14. Material / Item Master
15. Automatic Item Creation
16. Material Purchase Management
17. Vendor Purchase & Outstanding
18. Vendor Payments
19. Multi-Project Vendor Payment Allocation
20. Vendor Payment Allocation Example
21. Vendor Outstanding & Project Outstanding
22. No Duplicate Expense Rule
23. Vendor Payment Allocation History
24. Manual Vendor Allocation Override
25. Vendor Payment Greater Than Outstanding
26. Temple Donation Management
27. Customized / Ad-Hoc Work
28. Payment Mode Management





29. Cash & Bank Account Management
30. Project Budget & Cost Control
31. Budget Monitoring
32. Project Financial Ledger
33. Project Profit & Loss
34. Personal, Office & Savings Expenses
35. Common Expense Allocation Across Ongoing Projects
36. Common Expense Allocation Methods
37. Common Expense Allocation History
38. Loans & EMI
39. Project Reports
40. Vendor Reports
41. Vendor Payment Allocation Report
42. Subcontractor / Labour Reports
43. Temple Donation Reports
44. Loan Reports
45. Cash & Bank Reports
46. Company-Level Reports
47. Report Filters & Sorting
48. Role-Based Access Control
49. User Management
50. Role Management
51. Admin Configuration – Module Permissions
52. Granular Permissions
53. Accounts Team
54. Project-Level Access
55. Audit Trail
56. Notifications & Alerts
57. Document Attachments





- 58. Recommended Navigation
- 59. Phase-Wise Implementation
- 60. Key Business Rules
- 61. Overall Business Flow





1. Introduction

Livewires Digital Solutions proposes to develop a Construction Project Financial Management System for Colour Bricks.

The application will provide a centralized platform to manage multiple construction projects and track:

- Project income and credits
- Project expenses and debits
- Labour and subcontractor expenses
- Material purchases
- Vendors and vendor payments
- Temple donations
- Customized work
- Personal expenses
- Office expenses
- Savings
- Loans and EMIs
- Project-wise outstanding
- Vendor-wise outstanding
- Project profitability
- Budget versus actual cost
- Cash and bank transactions
- Multi-project vendor payment allocation
- Role-based access
- Management reports and dashboards

2. Business Objectives

The primary objectives are to:

1. Manage all construction projects from a single application.
2. Track project-wise income and expenses.





3. Monitor project profitability.
4. Compare project budget against actual expenses.
5. Identify cost overruns.
6. Manage labour and subcontractor teams.
7. Maintain centralized vendor and item masters.
8. Avoid repeatedly entering the same vendors and materials.
9. Track vendor purchases and outstanding balances.
10. Track payments to vendors and subcontractors.
11. Support daily, weekly, monthly and ad-hoc payments.
12. Track temple donations for each project.
13. Support multiple temples for a project.
14. Track customized work.
15. Support different payment modes.
16. Maintain cash and bank balances.
17. Track personal, office and savings expenses.
18. Allocate common expenses across ongoing projects.
19. Track project loans and EMI payments.
20. Automatically distribute consolidated vendor payments across projects.
21. Maintain accurate vendor and project outstanding balances.
22. Provide comprehensive reports with filtering and date ranges.
23. Provide configurable role-based permissions.
24. Maintain an audit trail for important financial activities.

3. Application Modules

The application will contain the following major modules:

1. Dashboard
2. Project Management
3. Project Income
4. Project Expense Management





5. Labour & Subcontractor Management
6. Vendor Management
7. Material/Item Management
8. Temple Donation Management
9. Customized Work Management
10. Payment Management
11. Cash & Bank Account Management
12. Budget & Cost Control
13. Project Profit/Loss
14. Personal Expenses
15. Office Expenses
16. Savings Management
17. Common Expense Allocation
18. Loan Management
19. EMI Management
20. Vendor Payment Allocation
21. Reports & Analytics
22. User Management
23. Role Management
24. Permission Management
25. Admin Configuration
26. Audit Trail

4. Project Management

A centralized Project Master will be maintained.

Project Details

- Project ID
- Project Name
- Client Name





- Site Address
- Contact Details
- Project Start Date
- Expected Completion Date
- Actual Completion Date
- Project/Contract Value
- Estimated Project Cost
- Expected Profit
- Project Status
- Project Manager
- Notes
- Attachments

Project Status

- Ongoing
- Completed
- On Hold
- Cancelled

Users will be able to view projects based on status.

5. Project Dashboard

When a user selects a project, the system should display a complete financial overview.

Summary

- Project Value
- Estimated Cost
- Actual Cost
- Total Income
- Total Expenses
- Total Paid
- Total Outstanding





- Current Balance
- Expected Profit
- Actual Profit
- Profit %
- Budget Utilisation %

Expense Breakdown

- Building Construction / Mesthri
- Interior
- Plumbing
- Electrical
- Materials
- Vendors
- Customized Work
- Temple Donations
- Personal/Common Expenses
- Office/Common Expenses
- Savings Allocation
- Loan/EMI
- Other Expenses

Users should be able to click summary figures and drill down into the underlying transactions.

6. Project Income / Credits

The system will allow users to record all income received against a project.

Examples:

- Client Advance
- Stage Payment
- Milestone Payment
- Additional Payment





- Final Payment
- Other Project Income

Transaction Details

- Project
- Transaction Date
- Transaction Type
- Amount
- Payment Mode
- Cash/Bank Account
- Reference Number
- Description
- Attachment
- Created By
- Created Date

7. Project Expenses / Debits

The system will track all expenses associated with a project.

Expense categories include:

- Labour
- Building Construction
- Interior
- Plumbing
- Electrical
- Materials
- Vendor Purchases
- Customized Work
- Temple Donation
- Common Expense Allocation
- Loan/EMI





- Other Expenses

8. Labour & Subcontractor Management

Multiple departments and multiple teams should be supported.

Initial Departments

- Mesthri / Building Construction
- Interior
- Plumbing
- Electrical

Additional departments can be created through administration.

Example

Electrical

- Electrical Team A
- Electrical Team B
- Electrical Team C

Plumbing

- Plumbing Team A
- Plumbing Team B

9. Subcontractor / Team Master

Each subcontractor/team can contain:

- Team/Subcontractor ID
- Name
- Department
- Contact Person
- Phone
- Email
- Address





- Payment Terms
- Bank Details
- Active/Inactive

A subcontractor/team can work on multiple projects.

10. Labour / Subcontractor Work

The system should record:

- Project
- Department
- Team/Subcontractor
- Work Type
- Work Description
- Work Date
- Agreed Work Value
- Amount Paid
- Outstanding Amount
- Payment Date
- Payment Mode
- Cash/Bank Account
- Reference
- Remarks

Payment Frequency

- Daily
- Weekly
- Monthly
- Milestone-based
- Ad-hoc

Outstanding

Outstanding = Agreed Work Value – Total Paid





11. Vendor Management

A centralized Vendor Master will be maintained.

Examples:

- Hardware Shops
- Cement Agencies
- Brick Agencies
- Sand Suppliers
- Steel Suppliers
- Plumbing Suppliers
- Electrical Suppliers
- Paint Suppliers
- Tile Suppliers
- Interior Suppliers
- Machinery Suppliers

A vendor should only need to be created once.

12. Vendor Master

Vendor information:

- Vendor ID
- Vendor Name
- Vendor Category
- Contact Person
- Phone
- Email
- Address
- GST Number
- Bank Details
- Payment Terms
- Active/Inactive





13. Automatic Vendor Creation

During the first transaction:

+ Add New Vendor

The vendor will automatically be added to the Vendor Master.

For subsequent transactions:

Search Vendor → Select Vendor

The system should provide:

- Search box
- Autocomplete
- Existing vendor list
- Add New Vendor option

Duplicate vendors should be prevented wherever possible.

14. Material / Item Master

A centralized Item Master will be maintained.

Examples:

- Cement
- Bricks
- Sand
- Steel
- Pipes
- Electrical Cables
- Switches
- Tiles
- Paint
- Doors
- Windows
- Hardware Items





- Plumbing Items
- Interior Materials

Item Details

- Item ID
- Item Name
- Category
- Unit
- Default Rate
- Tax/GST
- Active/Inactive

15. Automatic Item Creation

When entering a purchase:

Search Item

or

+ Add New Item

The first-time item will automatically be added to the Item Master.

Future users can simply search and select it.

16. Material Purchase Management

Material purchases should be recorded against projects.

Example:

Project A — Vendor: ABC Cement Agency

Item	Quantity	Rate	Amount
Cement	100 Bags	₹400	₹40,000
Sand	2 Loads	₹15,000	₹30,000
Total			₹70,000





Purchase information:

- Project
- Vendor
- Purchase Date
- Invoice Number
- Items
- Quantity
- Unit
- Rate
- Tax
- Total Amount
- Amount Paid
- Outstanding
- Payment Mode
- Account
- Reference
- Attachment



17. Vendor Purchase & Outstanding

Example:

Purchase:

₹2,00,000

Initial Payment:

₹50,000

Vendor Outstanding:

₹1,50,000

The system will maintain the complete purchase and payment history.





18. Vendor Payments

Vendor payments can be:

- Full
- Partial
- Daily
- Weekly
- Monthly
- Ad-hoc
- Multiple payments against a purchase

Example:

- Purchase = ₹2,00,000
- Payment 1 = ₹50,000
- Outstanding = ₹1,50,000
- Payment 2 = ₹75,000
- Outstanding = ₹75,000

19. Multi-Project Vendor Payment Allocation

A vendor may have outstanding balances across several projects.

The Accounts Team should be able to make one consolidated payment to a vendor, and the system should automatically distribute the payment across the relevant projects.

Default Method

FIFO – First In, First Out

The oldest outstanding balance will be settled first.

20. Vendor Payment Allocation Example

Vendor:

ABC Hardware





Project	Outstanding
Project A	₹25,000
Project B	₹10,000
Project C	₹30,000
Project D	₹50,000
Total	₹1,15,000

Vendor payment:

₹1,00,000

System allocation:

Project	Before	Allocated	After
Project A	₹25,000	₹25,000	₹0
Project B	₹10,000	₹10,000	₹0
Project C	₹30,000	₹30,000	₹0
Project D	₹50,000	₹35,000	₹15,000
Total	₹1,15,000	₹1,00,000	₹15,000

21. Vendor Outstanding & Project Outstanding

Before payment:

Vendor Outstanding = ₹1,15,000

Payment:

₹1,00,000

After payment:

Vendor Outstanding = ₹15,000

At the same time:

- Project A outstanding → ₹0
- Project B outstanding → ₹0
- Project C outstanding → ₹0





- Project D outstanding → ₹15,000

The vendor and project balances must remain synchronized.

22. No Duplicate Expense Rule

The system must distinguish between:

Purchase / Expense

and

Payment / Settlement

Example:

Purchase:

₹25,000

System records:

- Project Expense = ₹25,000
- Vendor Outstanding = ₹25,000

Later:

Vendor Payment = ₹25,000

System records:

- Vendor Outstanding = ₹0
- Cash/Bank reduces by ₹25,000
- Project payable reduces by ₹25,000

The payment must not create another ₹25,000 expense.

23. Vendor Payment Allocation History

Each consolidated payment should maintain allocation details.

Example:

Payment: ₹1,00,000





Project	Allocated
Project A	₹25,000
Project B	₹10,000
Project C	₹30,000
Project D	₹35,000
Total	₹1,00,000

Users should be able to view the complete allocation history.

24. Manual Vendor Allocation Override

Authorized users can manually override FIFO allocation where required.

Any manual override should be recorded in the audit trail.

25. Vendor Payment Greater Than Outstanding

Example:

Vendor Outstanding:

₹80,000

Payment:

₹1,00,000

Excess:

₹20,000

The excess should be recorded as:

Vendor Advance / Credit Balance

which can be adjusted against future purchases.

26. Temple Donation Management

Each project may have a percentage or fixed amount reserved for temple donations.

The system should support:





- Temple Master
- Multiple temples per project
- Percentage-based donation
- Fixed donation
- Donation allocation
- Donation payments
- Donation outstanding
- Payment Mode
- Cash/Bank Account
- Receipt/Reference

Example:

- Project Value = ₹1 Crore
- Donation = 2%
- Donation Amount = ₹2 Lakhs

The amount may be distributed across multiple temples.

27. Customized / Ad-Hoc Work

The system should support additional work not included in predefined work categories.

Examples:

- Additional construction
- Additional electrical work
- Additional plumbing
- Additional interior work
- Emergency work
- Client-requested changes
- Additional materials
- Additional labour

Information captured:

- Project





- Department
- Work Type
- Description
- Vendor/Subcontractor
- Estimated Cost
- Actual Cost
- Paid Amount
- Outstanding
- Date
- Payment Mode
- Account
- Reference

28. Payment Mode Management

Payment Mode will be maintained as a configurable master.

Initial modes:

- Cash
- Bank Transfer
- UPI
- Cheque
- Credit Card
- Debit Card
- Online Transfer
- Other

Payment Mode will be available across:

- Project Income
- Vendor Payments
- Labour Payments
- Subcontractor Payments





- Temple Donations
- Personal Expenses
- Office Expenses
- Savings
- Loan EMI
- Other Transactions

29. Cash & Bank Account Management

The system should support multiple accounts.

Cash

- Office Cash
- Site Cash

Bank

- HDFC
- SBI
- ICICI
- Other Bank Accounts

Every applicable financial transaction should record:

Payment Mode + Account

30. Project Budget & Cost Control

Each project should have an estimated/approved cost.

The system will continuously compare:

Estimated Cost vs Actual Cost

Example:

- Estimated Cost = ₹80,00,000
- Actual Cost = ₹82,00,000

The system should show:





Budget Exceeded by ₹2,00,000

31. Budget Monitoring

Expenses should be monitored by category.

Category	Budget	Actual	Variance
Labour	₹20L	₹19L	₹1L
Materials	₹35L	₹38L	₹3L Over
Electrical	₹5L	₹6L	₹1L Over

Suggested status:

- Within Budget
- Approaching Budget
- Budget Exceeded

Thresholds should be configurable.

32. Project Financial Ledger

Each project should have a complete credit/debit ledger.

Date	Description	Credit	Debit	Balance
01-Aug	Client Advance	₹10L	-	₹10L
03-Aug	Cement Purchase	-	₹1L	₹9L
05-Aug	Labour Payment	-	₹50K	₹8.5L
07-Aug	Electrical Work	-	₹40K	₹8.1L
10-Aug	Client Payment	₹5L	-	₹13.1L

Each transaction should be clickable for detailed information.

33. Project Profit & Loss

Basic calculation:

Project Profit = Project Revenue – Project Costs





The system will display:

- Project Revenue
- Estimated Cost
- Actual Cost
- Gross Profit
- Profit %
- Budget Variance

34. Personal, Office & Savings Expenses

The system should support:

Personal Expenses

- Personal withdrawals
- Personal purchases
- Other personal expenses

Office Expenses

- Office rent
- Electricity
- Internet
- Salaries
- Stationery
- Travel
- Software
- Maintenance

Savings

- Savings allocation
- Savings transactions

35. Common Expense Allocation Across Ongoing Projects





Personal Expenses, Office Expenses and Savings will be treated as common/company-level expenses.

The system should allow the total amount to be distributed among ongoing projects.

Default Allocation Method

Equal Distribution

Formula:

$$\text{Project Allocation} = \text{Total Common Expense} \div \text{Number of Ongoing Projects}$$

Completed, cancelled and on-hold projects will be excluded.

Example

For a particular period:

Expense Type	Amount
Personal Expenses	₹40,000
Office Expenses	₹35,000
Savings	₹25,000
Total	₹1,00,000

Suppose there are four ongoing projects:

Project	Allocation	Amount
Project A	25%	₹25,000
Project B	25%	₹25,000
Project C	25%	₹25,000
Project D	25%	₹25,000
Total	100%	₹1,00,000

If there are five ongoing projects:

$$₹1,00,000 \div 5 = ₹20,000 \text{ per project}$$

36. Common Expense Allocation Methods





The system should support:

1. Equal Distribution

Total amount ÷ number of ongoing projects.

2. Percentage Based

Example:

Project	Allocation
Project A	40%
Project B	30%
Project C	20%
Project D	10%

3. Manual Distribution

Accounts/Admin can manually specify the amount for each project.

Default

Equal Distribution

37. Common Expense Allocation History

Every allocation should maintain:

- Original Expense
- Expense Type
- Total Amount
- Allocation Method
- Projects
- Allocated Amount
- Allocation Date
- Created By

This allows management to trace how common expenses were distributed.





38. Loans & EMI

Projects may be financed through loans.

Loan Master

- Loan ID
- Project
- Bank/Lender
- Loan Amount
- Interest Rate
- Start Date
- Tenure
- EMI Amount
- EMI Start Date
- EMI End Date
- Outstanding Principal
- Status

EMI

- Project
- Loan
- EMI Date
- EMI Amount
- Principal
- Interest
- Payment Mode
- Account
- Reference
- Status

Reports:

- Total Loan





- Principal Paid
- Interest Paid
- Outstanding Principal
- Upcoming EMI
- Overdue EMI

39. Project Reports

Project Financial Summary

- Project Value
- Estimated Cost
- Actual Cost
- Income
- Expenses
- Profit/Loss
- Profit %

Project Expense Report

Filters:

- Project
- Category
- Department
- Vendor
- Subcontractor
- Payment Mode
- Account
- Date Range

Project Ledger

Complete credit/debit history.

Budget vs Actual





- Budget
- Actual
- Variance
- Variance %

Project Labour Report

Department/team-wise cost.

Project Material Report

- Item
- Quantity
- Rate
- Amount
- Vendor
- Date

Project Outstanding

- Vendor Outstanding
- Subcontractor Outstanding
- Loan Outstanding
- Other Outstanding

40. Vendor Reports

The system should provide:

Vendor Statement

- Purchases
- Payments
- Allocations
- Advances
- Outstanding

Vendor Purchase Report





- Vendor
- Project
- Item
- Category
- Date

Vendor Payment Report

Complete payment history.

Vendor Outstanding Report

- Total Purchases
- Total Paid
- Outstanding

Vendor Project-wise Statement

Vendor	Project	Purchase	Paid	Outstanding
ABC	Project A	₹2L	₹1.5L	₹50K
ABC	Project B	₹1L	₹50K	₹50K

41. Vendor Payment Allocation Report

This report should show how one vendor payment was distributed.

Date	Vendor	Total Payment	Project	Allocated
26-Aug	ABC Hardware	₹1L	Project A	₹25K
26-Aug	ABC Hardware	₹1L	Project B	₹10K
26-Aug	ABC Hardware	₹1L	Project C	₹30K
26-Aug	ABC Hardware	₹1L	Project D	₹35K

42. Subcontractor / Labour Reports

Reports should include:

- Subcontractor Statement
- Department-wise Expense





- Team-wise Expense
- Project-wise Team Expense
- Payment History
- Outstanding Report
- Work Value vs Payment
- Date-wise Payment Report

43. Temple Donation Reports

- Project-wise Donation
- Temple-wise Donation
- Donation Percentage
- Donation Allocated
- Donation Paid
- Donation Outstanding
- Date-wise Donation


44. Loan Reports

- Project-wise Loans
- Loan Outstanding
- EMI Schedule
- EMI Paid
- EMI Pending
- Principal vs Interest
- Date-wise EMI Payments

45. Cash & Bank Reports

Account Statement

- Opening Balance
- Credits

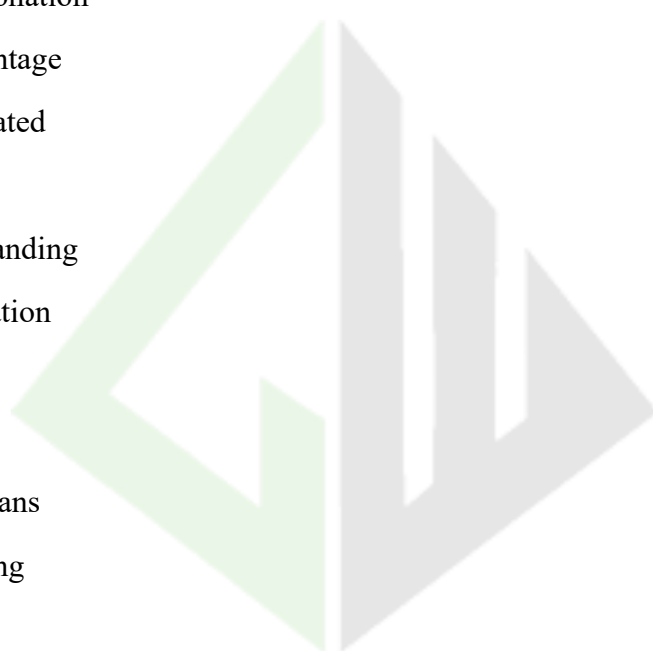



- Debits
- Closing Balance

Payment Mode Report

Payment Mode	Received	Paid
Cash	₹5L	₹3L
Bank Transfer	₹20L	₹15L
UPI	₹4L	₹2L
Cheque	₹2L	₹1L

Bank-wise Report

Transactions grouped by bank account.

46. Company-Level Reports

Management reports:

- Overall Income
- Overall Expenses
- Overall Profit/Loss
- Ongoing Projects
- Completed Projects
- Project-wise Profitability
- Vendor Outstanding
- Subcontractor Outstanding
- Loan Outstanding
- Cash Position
- Bank Position
- Expense Category Analysis
- Monthly Income vs Expense
- Monthly Profit/Loss
- Common Expense Allocation





47. Report Filters & Sorting

Reports should support:

Filters

- Project
- Vendor
- Subcontractor
- Department
- Item
- Category
- Payment Mode
- Account
- Payment Status
- Transaction Type
- Date From
- Date To

Date Filters

- Today
- Yesterday
- This Week
- Previous Week
- This Month
- Previous Month
- Current Year
- Previous Year
- Custom Date Range

Functions

- Search
- Sort





- Pagination
- Column selection
- Grouping
- Export to Excel
- Export to PDF
- Print
- Reset Filters

48. Role-Based Access Control

The application will implement:

User → Role → Module → Action

Optional:

User → Role → Project Access

49. User Management

Administrator should be able to:

- Add User
- Edit User
- Activate User
- Deactivate User
- Delete User where permitted
- Assign Role
- Assign Projects
- Reset access

User Details

- Name
- Username/Email
- Mobile





- Role
- Department
- Status
- Assigned Projects

50. Role Management

Administrator should be able to:

- Add Role
- Edit Role
- Activate/Deactivate Role
- Delete Role where permitted
- Configure Permissions
- Assign Users

Suggested Roles

Administrator

Full access.

Accounts Team

Financial data entry/update.

Project Manager

Project-related access.

Management

Dashboard and reporting.

Data Entry User

Limited data entry.

Additional roles can be created.

51. Admin Configuration – Module Permissions





A dedicated:

Admin → Role & Permission Configuration

page will allow administrators to enable/disable modules for each role.

Example:

Accounts Team

Enabled:

- Projects
- Project Income
- Project Expenses
- Vendors
- Materials
- Labour/Subcontractors
- Temple Donations
- Payments
- Loans
- Reports

Disabled:

- User Management
- Role Management
- System Configuration

If a module is disabled, it should not be visible in the user's menu.

52. Granular Permissions

Each module should support:

- View
- Add
- Edit
- Delete





- Approve
- Export
- Print

Example:

Module	View	Add	Edit	Delete	Approve	Export
Projects	✓	✓	✓	✗	✓	✓
Vendors	✓	✓	✓	✗	✗	✓
Materials	✓	✓	✓	✗	✗	✓
Expenses	✓	✓	✓	✗	✓	✓
Payments	✓	✓	✓	✗	✓	✓
Reports	✓	✗	✗	✗	✗	✓
Users	✓	✓	✓	✓	✗	✗
Roles	✓	✓	✓	✓	✗	✗

Actual permissions will be configurable by the Administrator.

53. Accounts Team

Accounts users may have access to:

- Project Income
- Project Expenses
- Vendor Purchases
- Vendor Payments
- Vendor Payment Allocation
- Subcontractor Payments
- Temple Donations
- Personal Expenses
- Office Expenses
- Savings





- Loan Transactions
- EMI Payments
- Payment Modes
- Cash/Bank Transactions
- Financial Reports

The Administrator can change these permissions.

54. Project-Level Access

Users may optionally be restricted to selected projects.

Example:

Project Manager A

Can access:

- Project A
- Project B

Cannot access:

- Project C
- Project D



55. Audit Trail

Important activities should be logged.

Audit information:

- User
- Date/Time
- Module
- Action
- Record ID
- Old Value
- New Value





Examples:

- User edited Vendor Payment VP1024.
- Admin changed Accounts Team permissions.

Financial transactions should preferably use:

- Cancel
- Reverse
- Void

instead of permanent deletion.

56. Notifications & Alerts

The system may notify users when:

- Project budget is exceeded
- Project approaches budget
- Vendor payment is overdue
- Subcontractor payment is overdue
- EMI is due
- EMI is overdue
- Project profitability falls below threshold
- Vendor outstanding reaches a configured limit

Notifications can be:

- Dashboard
- Email
- Both

57. Document Attachments

Users should be able to attach:

- Vendor Invoice
- Purchase Bill





- Payment Receipt
- Bank Transfer Proof
- Cheque Copy
- Donation Receipt
- Loan Documents

58. Recommended Navigation

Dashboard

- Company Dashboard
- Project Dashboard

Projects

- Ongoing Projects
- Completed Projects
- Project Master
- Project Ledger
- Project Income
- Project Expenses
- Project Budget
- Project Profit/Loss

Vendors

- Vendor Master
- Purchases
- Payments
- Outstanding
- Statements
- Payment Allocation

Labour / Subcontractors

- Departments





- Teams
- Work Entries
- Payments
- Outstanding
- Statements

Materials

- Item Master
- Item Categories
- Purchases

Temple Donations

- Temple Master
- Project Donations
- Donation Payments
- Reports

Loans

- Loan Master
- EMI Schedule
- EMI Payments
- Outstanding

Other Expenses

- Personal Expenses
- Office Expenses
- Savings
- Common Expense Allocation
- Customized Expenses

Accounts

- Cash Accounts
- Bank Accounts





- Payment Modes
- Transactions

Reports

- Project Reports
- Vendor Reports
- Subcontractor Reports
- Material Reports
- Donation Reports
- Loan Reports
- Cash/Bank Reports
- Profit/Loss
- Outstanding
- Budget vs Actual
- Common Expense Allocation

Administration

- Users
- Roles
- Permissions
- Module Configuration
- Masters
- Audit Logs
- System Settings

59. Phase-Wise Implementation

Phase 1 – Core Project Financial Management

- Project Management
- Project Dashboard
- Project Income
- Project Expenses





- Budget vs Actual
- Project Profit/Loss
- Vendor Master
- Material Master
- Vendor Purchases
- Vendor Outstanding
- Labour/Subcontractor Management
- Temple Donations
- Customized Work
- Payment Modes
- Cash/Bank Accounts
- User Management
- Role Management
- RBAC
- Admin Configuration
- Audit Trail
- Basic Reports

Phase 2 – Additional Expenses

- Personal Expenses
- Office Expenses
- Savings
- Common Expense Allocation
- Equal distribution
- Percentage-based distribution
- Manual distribution
- Allocation history
- Additional reports

Phase 3 – Loans & EMI

- Loan Master





- Project Loans
- EMI Schedule
- EMI Payments
- Principal Tracking
- Interest Tracking
- Outstanding Loan
- EMI Alerts
- Loan Reports

Phase 4 – Advanced Vendor Payment Allocation

- Consolidated Vendor Payment
- Multi-project allocation
- FIFO allocation
- Partial allocation
- Full allocation
- Vendor advance
- Manual override
- Allocation history
- Project-wise outstanding update
- Vendor outstanding update
- Project ledger settlement
- Cash/Bank update
- Audit trail
- Allocation reports

Phase 5 – Advanced Reporting & Analytics

- Advanced Project Reports
- Vendor Analytics
- Subcontractor Analytics
- Project Profitability
- Cash Flow





- Bank-wise Reports
- Expense Trends
- Monthly/Annual Comparison
- Advanced Dashboards
- Excel Export
- PDF Export
- Advanced Filtering
- Additional Management Reports

60. Key Business Rules

1. Every project must have a unique Project ID.
2. Every project should have an estimated/approved cost.
3. Financial transactions should be associated with the appropriate project.
4. One project can have multiple vendors.
5. One vendor can work across multiple projects.
6. One project can have multiple subcontractors.
7. One subcontractor can work across multiple projects.
8. One project can have multiple departments.
9. One department can have multiple teams.
10. Multiple temples can be associated with one project.
11. Temple donations can be percentage-based or fixed.
12. Partial payments must be supported.
13. Multiple payments against one purchase must be supported.
14. New vendors can be created during transaction entry.
15. New items can be created during transaction entry.
16. Existing vendors and items must be searchable.
17. Duplicate vendors/items should be prevented wherever possible.
18. Applicable payments must record Payment Mode.
19. Applicable payments must record Cash/Bank Account.





20. Project budget must be continuously compared against actual cost.
21. Budget overruns must be highlighted.
22. Vendor payments must support automatic multi-project allocation.
23. FIFO should be the default allocation method.
24. Authorized users may override automatic allocation.
25. Vendor-level outstanding must be updated after allocation.
26. Project-level outstanding must be updated after allocation.
27. Project ledger must reflect settlement.
28. Vendor payment must not create a duplicate expense.
29. Vendor payment allocation history must be maintained.
30. Vendor advances must be supported.
31. Completed projects must remain available for historical reporting.
32. Financial transactions should preferably be cancelled/reversed rather than permanently deleted.
33. Reports must support date filtering.
34. Reports must support searching and sorting.
35. User permissions must control module and action access.
36. Administrators must be able to configure permissions.
37. Project-level access should be supported.
38. Personal, Office and Savings expenses should initially be treated as common expenses.
39. Common expenses should be allocated only to ongoing projects.
40. Equal distribution should be the default common expense allocation method.
41. Percentage and manual allocation should also be supported.
42. Common expense allocation history must be maintained.

61. Overall Business Flow

Project Creation





Project Value & Budget



Project Income / Credits



Project Work



Material Purchases



Vendor Outstanding



Labour / Subcontractor Expenses



Customized Work



Temple Donations



Personal / Office / Savings



Common Expense Allocation



Loans / EMI



Vendor / Subcontractor Payments



Multi-Project Vendor Payment Allocation



Cash / Bank Update





Project Outstanding Update



Budget vs Actual



Project Profit / Loss



Reports & Analytics

Prepared By:

Livewires Digital Solutions

Prepared For:

Colour Bricks

